

## PROFORMA FOR SAFE DRINKING WATER AND SANITARY CONDITION CERTIFICATE

No. 389Dated: 08/07/2025

It is certified that an inspection team headed by Nilesh Chhatrapale,  
(Name of Officers with designation) from Chemist, P.H.E.D. Betul (M.P.)

PHED inspected the **Corolla Public School, Bhagat Singh Ward, Multai, Dist Betul, (M.P)** on 08/07/2025

and on the basis of Water Test Report (Attached) bearing no. TC12083240000000000334F

dated 08/07/2025 of District Water Testing Laboratory P.H.E.D. Betul

(PHED Lab) certified that the **Corolla Public School, Bhagat Singh Ward, Multai, Dist Betul, (M.P)** has safe drinking water facilities for the students and members of staff of the institution. School is also maintains the hygienic sanitation condition in the school building & the campus as per norms prescribed by the Central/

State/ U.T. Govt.

This certificate is valid till 06 Months

Signature with seal



Name

Designation

:- Public Health Engineering Deppt.  
Betul (M.P.)

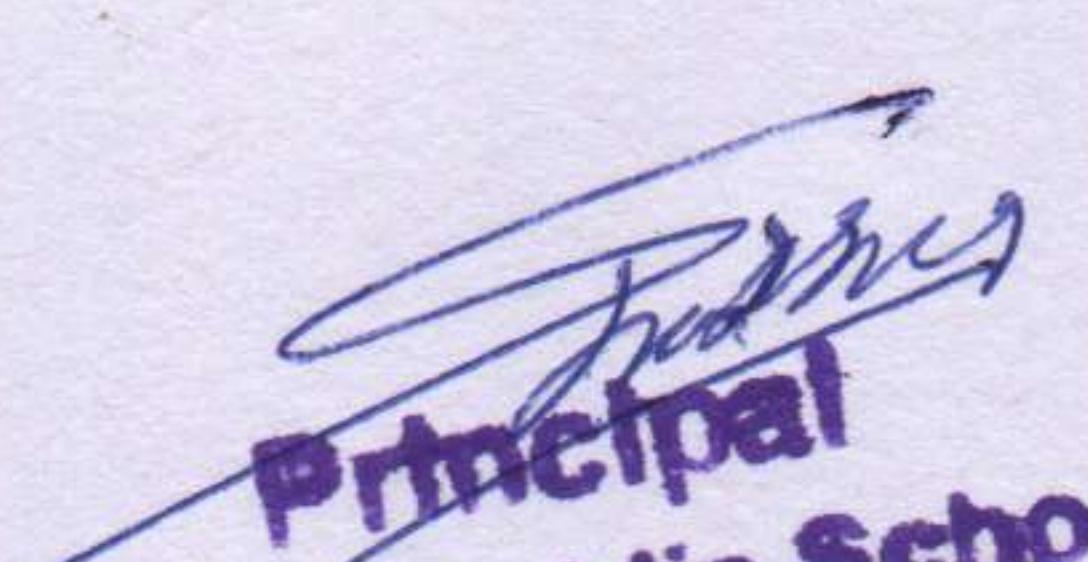
:- Nilesh Chhatrapale

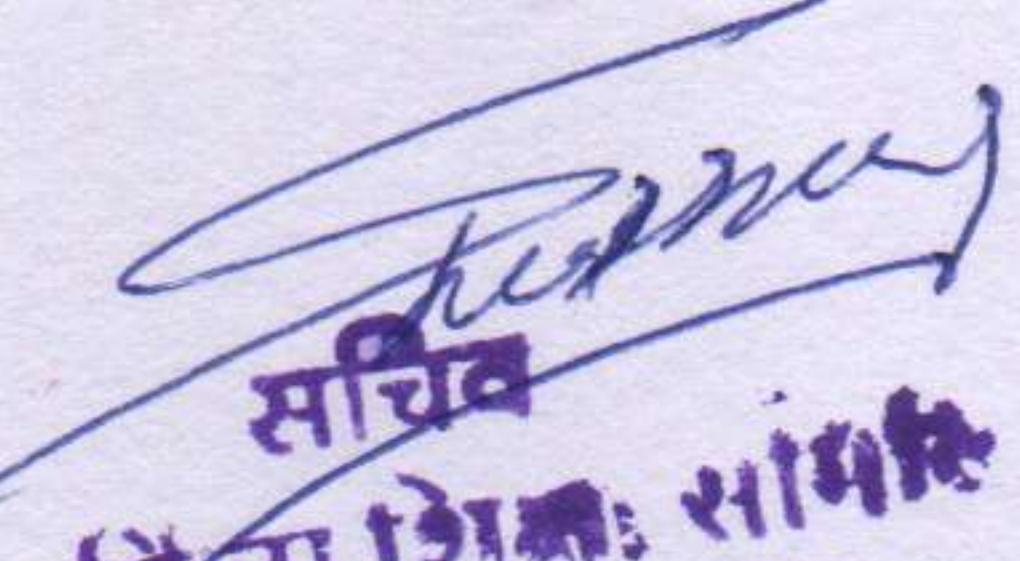
:- Chemist

  
Assistant Engineer  
P.H.E. Sub Division  
Multai Dist. Betul

Name & address of the office/Department :- Public Health Engineering  
Department Betul (M.P.)

To,  
**Corolla Public School,**  
**Bhagat Singh Ward, Multai, Dist Betul, (M.P)**  
(Name and address of the institution)

  
Principal  
**Corolla Public School**  
**Multai**

  
Sanitary  
Engineer  
Dwari Gram Panchayat

Note: The certificate is to be issued by authorized officer / PHED Lab/local bodies

**DISTRICT WATER TESTING LABORATORY**  
**Public Health Engineering Department P.H.E.D Betul**  
**Near Satpuda club, Sadar, Betul (M.P.) 460001**



TC-12083

**TEST REPORT**

Location of Performance Testing :- Laboratory				
Nature of sample:- Drinking Water Sample/Others		Not sampled by Lab	Unique Identification No.	DWTLBET
To COROLLA PUBLIC SCHOOL MULTAI DISTT. BETUL (M.P.)	Sender letter no.	531	Sender's letter Date	7/7/2025
	Date of receiving sample	7/7/2025	Collection date of sample	7/7/2025
	Lab Ref. No	289	Lab Ref. Date	7/7/2025
	Date of Analysis started	7/7/2025	Date of Analysis Completed	8/7/2025
	Quantity of sample	1 LTR	URL No- TC120832400000 00000334F	

**SAMPLE DETAILS**

NO.	Particulars of Samples
1	R.O. Water Sample
2	_____

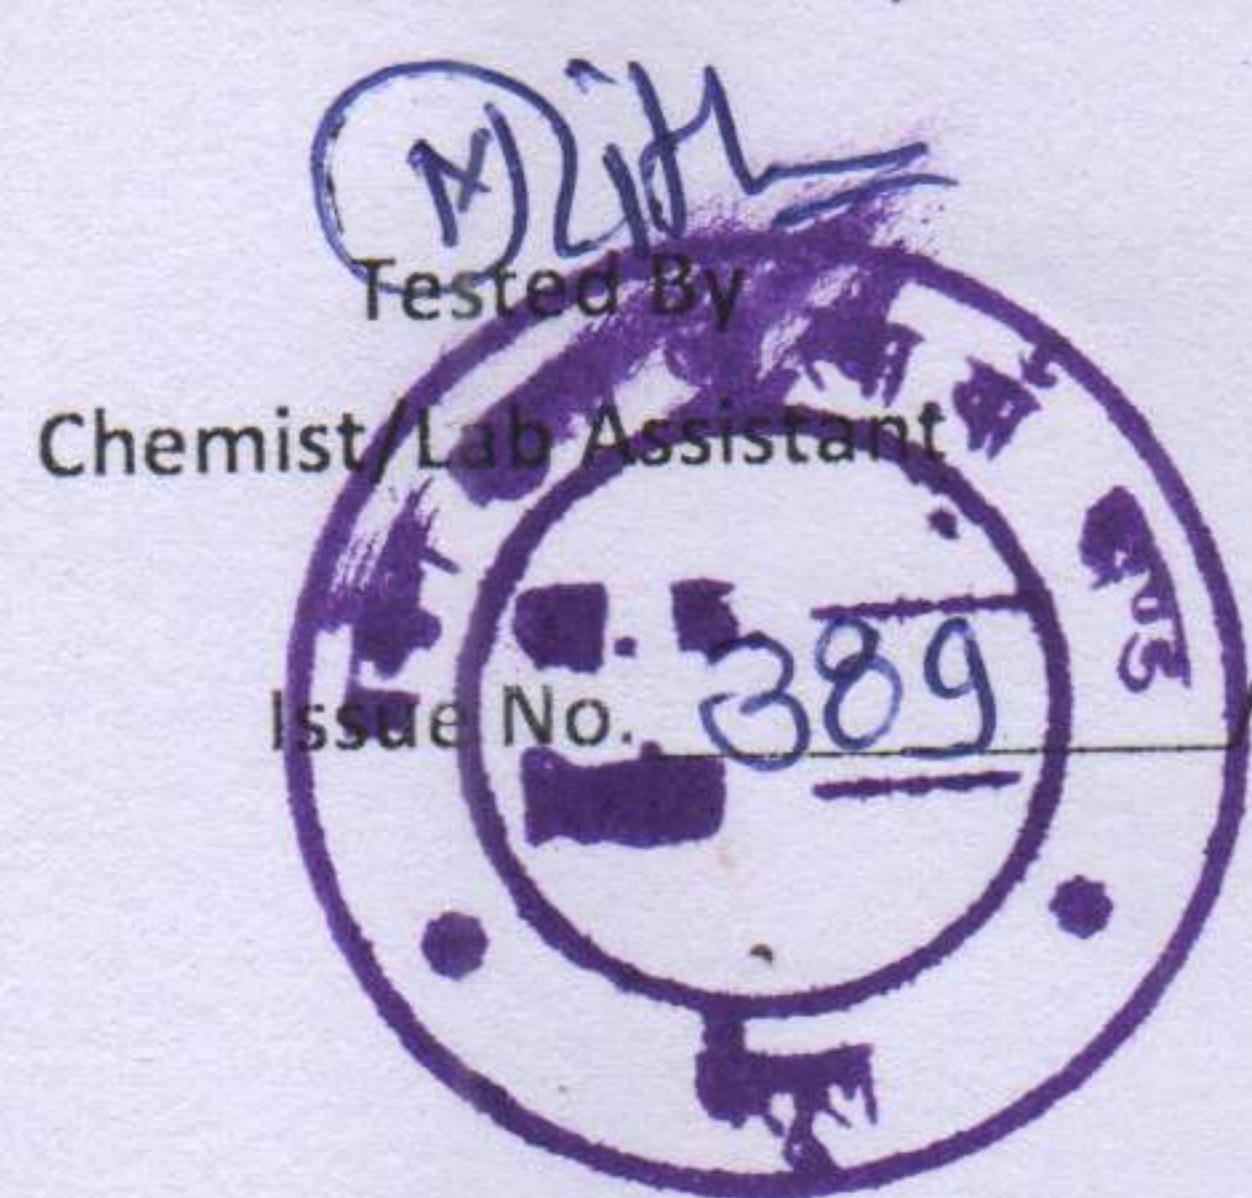
**RESULTS**

No.	Characteristics	Unit	Test methods	BIS-10500:2012 Reaffirmed in Sep. 2018		Results	
				4	Desirable Limit	Permissible Limit	1
1	2	3	BIS:3025 part 8	5	6		2
1	Taste		BIS:3025 part 4	Aggregable	Aggregable	Agg	-
2	Colour in	Hazen scale	BIS:3025 part 5	5	15	7	-
3	Odour	-	BIS:3025 part 32	Aggregable	Aggregable	Agg.	-
4	Chloride as Cl	mg/l	BIS:3025 part 23	250	1000	78	-
5	Total Alkalinity as CaCO <sub>3</sub>	mg/l	BIS:3025 part 40	200	500	180	-
6	Calcium as Ca++	mg/l	BIS:3025 part 46	75	200	4.8	-
7	Magnesium as Mg++	mg/l	BIS:3025 part 21	30	100	37.01	-
8	Total Hardness as CaCO <sub>3</sub>	mg/l	BIS:3025 part 11	200	600	164	-
9	pH	pH scale	BIS:3025 part 60	6.5 to 8.5	6.5 to 8.5	7.49	-
10	Fluoride as F	mg/l	BIS:3025 part 24	1.0	1.5	0.39	-
11	Sulphate as SO <sub>4</sub>	mg/l	BIS:3025 part 10	200	400	19.8	-
12	Turbidity	NTU	BIS:3025 part 14	1.0	5.0	1.3	-
13	Conductivity at 25°C	micromhos/cm	BIS:3025 part 16	-	-	487	-
14	TDS	mg/l	BIS:3025 part 26	500	2000	292	-
15	R.Chlorine	mg/l	BIS:3025 part 26	0.01	0.2	0.01	-

**Disclaimer**

1. This report should not be produced partly or full without approval of signatory authority for legal purposes.
2. It is recommended that acceptable limit is to be implemented. Values in excess of those mentioned under "acceptable" render the water not suitable, but still may be tolerated in the absence of an alternative source but the limit indicated under the "permissible limit in the absence of alternate source" in column 6, above with the sources will have to be rejected.
3. The results refer only to tested sample and parameters tested.
4. Samples will be stored for a period of 15 days from the date of issue of report.
5. This lab does not hold any responsibility for variation in results for samples kept on hold for want of clarification.

End of the test report



*Shenck*  
 Reviewed by  
 Technical Manager

*A. S. J.*  
 AUTHORIZED SIGNATORY  
 Quality Manager

DWTL/PHED/BET/ Issue Date 08/7/25
